RE-ENVISIONING DOYLE DRIVE

PRESIDIO PARKWAY

Project Update

California Transportation Commission

Thursday June 25 , 2015

Two Phases – DBB & P3

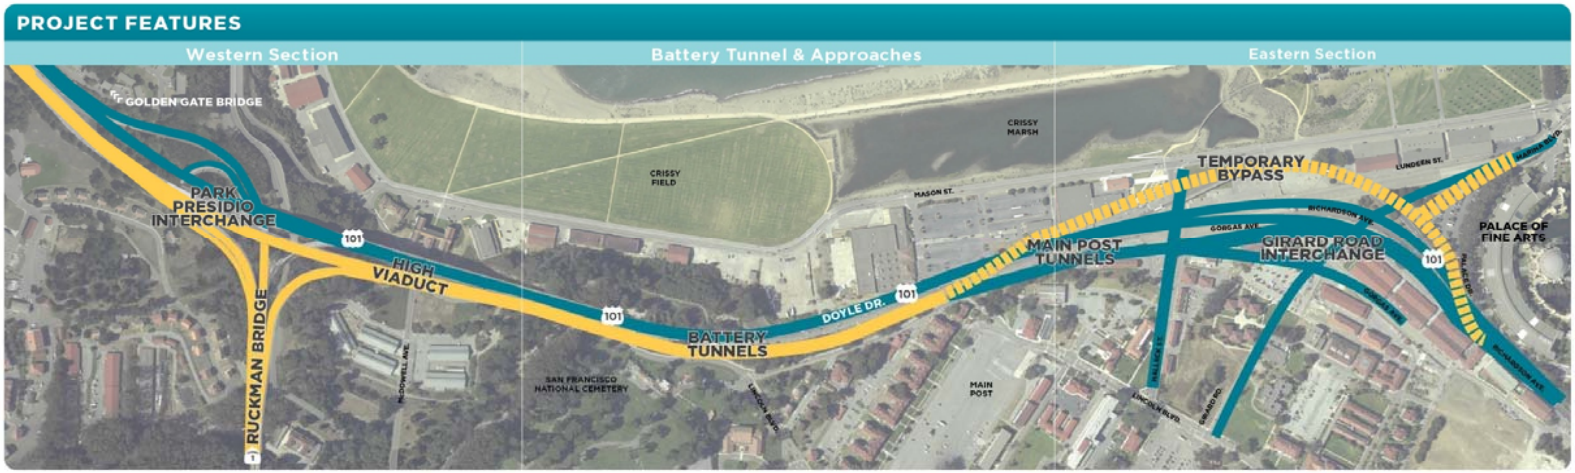

Existing Facility Prior to Construction

Phase 1 Detour Stage - DBB

Presidio Parkway

High Viaduct 101 /1 Interchange– Jun 3, 2015

High Viaduct NB 101

At-Grade Section between Battery Tunnels and Main Post Tunnels– Jun 3, 2015

Main Post Tunnels & Tennessee Hollow Bridges

Main Post Tunnels – Jun 3, 2015

NB 101 Mainline / Retaining Wall 117

Girard Interchange Undercrossing – Jun 3, 2015

Girard Interchange Undercrossing

CTC Tour – May 18, 2015

Transportation. All Rights Reserved

July 9, 2015 Weekend Traffic Switch Details

- Full Closure of Doyle Drive
- Golden Gate Bridge, NB 1 and SB 1 will remain open
- Mason Steet in the Presidio will remain open
- Closure Start Time: 10:00 PM on Thursday July 9th
- Pickup Time: 5:00 AM on Monday July 13th
- 79 hour construction schedule
- 4 Primary Work Locations
- Critical Paths – Mainline 101 CRCP between Main Post and Battery Tunnels and Richardson Tie-In
- There are large grade differences at Richardson and along the mainline. The work cannot be split into two weekends.

Traffic Switch Primary Work Areas

Toll Plaza

Girard I/C

Mainline CRCP

Richardson

Project Schedule

Completion of Contracts 1-4	Fall 2012
CTC vote to adopt P3	5/20/2010
P3 Agreement Executed	1/07/2011
Notice to Proceed 1 – Design	4/01/2011
Financial Close	6/24/2012
Notice to Proceed 3 – Construction	11/06/2012
Notice to Proceed 2 – O&M during Construction	3/08/2013
Traffic Switch	7/09/2015 to 7/13/2015
Substantial Completion	9/24/2015
Final Acceptance	9/23/2016
Milestone Payment Due	45 days after Substantial Completion
O&M Phase (30 year term)	9/24/2015 to 9/24/2045

TN5

Slide 17

TN5 Substantial Completion – 9/24/15 per approved Proj Sched dated 6/15/12
Acceptance – 10/28/15 per approved Proj Sched dated 6/15/12
Milestone Payment – 11/9/15 (45 days after Substantial Completion per P3 agreement 4.9.4.2)
O&M Phase – 9/24/15 (per P3 Agreement Appendix A – Definition of O&M Period)
O&M Completion – 9/24/45 (30 yrs after Substantial Completion per P3 agreement 2.2.1)
Tuqan, Nidal@DOT, 6/22/2015

QUESTIONS?
